

**The Consolidated Report of Activities
for the Quarter Ended March 31, 2026**

For

The Stipulated Order on Sewer System (CWA Case)
as Entered on September 30, 2023

By United States District Judge Henry T. Wingate

In Case Number 3:12-cv-790-HTW-LGI

The United States and the State of Mississippi

v

The City of Jackson, Mississippi

April 30, 2026

Prepared by Edward “Ted” Henifin, P.E.

The Interim Third-Party Manager

Of the City of Jackson’s Drinking Water and Sewer Systems

Table of Contents

List of Figures ii

List of Tables..... iii

Executive Summary 1-1

Introduction and Purpose 1-2

Section 1: Summary Tables of Sanitary Sewer Overflows and Bypasses 1-2

1.1 Sanitary Sewer Overflows (SSOs)..... 1-2

1.2 Prohibited Bypasses 1-2

Section 2: Narrative Report 2-3

2.1 Projects and Activities..... 2-3

Management, Operations and Maintenance (MOM) Plans 2-3

2.2 Delays 2-3

2.3 Sewer Project Priority List and Implementation Schedule 2-4

2.4 Accounting of Expenditures..... 2-5

2.5 Projection of Work for Upcoming Quarter..... 2-7

2.6 Supplemental Environmental Program (SEP) 2-7

2.7 Trends Analysis 2-7

Appendix A: Collection System SSO Data..... A-1

Appendix B: White Oak (Frontage Road) SSO Photograph B-1

List of Figures

Figure 2-1. Number of Municipally Owned Sanitary Sewer Overflows by Month 2-7

Figure 2-2. Total Volume of Municipally Owned Sanitary Sewer Overflows by Month 2-8

Figure 2-3. Average Duration of Sanitary Sewer Overflows by Month 2-8

Figure 2-4. Causes of Municipally Owned Sanitary Sewer Overflows during 2024-2025 2-9

Figure 2-5. Causes of Municipally Owned Sanitary Sewer Overflows by Month..... 2-9

Figure 2-6. Causes of Prohibited Bypass Events by Month 2-10

Figure 2-7. Total Estimated Volume of Prohibited Bypass Events by Month..... 2-10

Figure 2-8. Total Duration of Prohibited Bypass Events by Month..... 2-11

List of Tables

Table 1. JXN Water Master Schedule for Priority Projects 2-4

Table 2. JXN Water Expenditures vs. Budget for FY25 2-6

Table A-1. Municipally Owned January Collection System SSOs which Reached Waters of the State A-1

Table A-2. Municipally Owned January Collection System SSOs which Did Not Reach Waters of the State... A-1

Table A-3. January Frontage Rd Collapse SSO Details..... A-2

Table A-4. Privately Owned January Collection System SSOs..... A-2

Table A-5. January West Bank Interceptor (WBI) SSOs A-4

Table A-6. Municipally Owned February Collection System SSOs which Reached Waters of the State A-4

Table A-7. Municipally Owned February Collection System SSOs which Did Not Reach Waters of the State . A-4

Table A-8. February Frontage Rd Collapse SSO Details..... A-5

Table A-9. Privately Owned February Collection System SSOs A-5

Table A-10. Municipally Owned March Collection System SSOs which Reached Waters of the State A-6

Table A-11. Municipally Owned March Collection System SSOs which Did Not Reach Waters of the State... A-7

Table A-12. March Frontage Rd Collapse SSO Details..... A-7

Table A-13. Privately Owned March Collection System SSOs..... A-8

Table A-14. March Pump Station SSOs..... A-9

Executive Summary

JXN Water made substantial progress on sewer system issues in the First Quarter of 2026. These accomplishments included:

1. Resolving 47 SSOs occurring in the quarter on municipally owned assets.
2. Cleaning and televising 105,478 linear feet of sewer mains this quarter. This brings the cumulative total up to 1,394,733 linear feet since the effective date of the Stipulated Order.

There was an extraordinary SSO which continued this quarter: a pipe collapse at Frontage Road. At this location, wastewater was exiting the pipe, flowing along the route and re-entering the pipe. It appears that the underlying cause is an ongoing slope failure outside the utility right of way. JXN Water is evaluating long term solutions to this failure location. See Appendix B: for a photograph of the sewer failure site.

There is also an ongoing SSO at Livingston Street at the site of the Mill Street Gravity Replacement Project. That project is on hold pending funding.

JXN Water remains committed to improving the performance of the sewer system, including the treatment plants. We continue to seek funding to support these improvements. At this time, all scheduled commitments are subject to change because of the delay in enacting a rate increase necessary to support the financing for capital improvements. Although the rate increase has been approved, it will take time to increase revenues sufficiently to support the needed capital program.

Introduction and Purpose

This Quarterly Sewer Status Report has been prepared pursuant to Section 17 of the Stipulated Order entered on 9/30/2023, which states that the ITPM shall submit to the Parties and file on the Court's docket written status reports on its progress in implementing the Stipulated Order.

All of the planned work described below is dependent upon having adequate resources to perform the work. This will require a suite of funding options, including a rate increase, the ability to borrow funds, etc.

Section 1: Summary Tables of Sanitary Sewer Overflows and Bypasses

1.1 Sanitary Sewer Overflows (SSOs)

The Jackson sanitary sewer system has seen significant improvements, but it will take time to rehabilitate after decades of neglect. We not only have addressed the hundreds of sewer defects and overflows that were previously ignored, but we are keeping up with newly identified overflows and defects.

In Appendix A, Table A-1, Table A-6, and Table A-10 summarize the sanitary sewer overflows from the Jackson collection system that reached waters of the state during January, February, and March, respectively. Waters of the state are defined by Mississippi law as "all waters within the jurisdiction of the State of Mississippi, including all streams, lakes, ponds, impounding reservoirs, wetlands, water-courses, waterways, wells, springs, irrigation systems, drainage systems, and all other bodies or accumulations of water, surface and underground, natural or artificial, situated wholly or partly within or bordering upon the state, and such coastal waters as are within the jurisdiction of the state, except lakes, ponds, or other surface waters that are wholly landlocked and privately owned and not regulated under the federal Clean Water Act." Table A-2, Table A-7, and Table A-11 summarize the sanitary sewer overflows from the municipally owned collection system that did not reach waters of the state.

Also attached are Table A-4, Table A-9, and Table A-13, which summarize 93 new overflows that have occurred from privately-owned sewer laterals. 77 of these overflows, approximately 83% are ongoing. It is also likely that private lateral overflows reported in prior quarterly reports remain ongoing. JXN Water is not responsible for these overflows. Instead, the Mississippi DEQ and City of Jackson are responsible for resolving these unpermitted private sewer lateral releases. JXN Water has provided timely notice to the Mississippi DEQ of these overflows.

Table A-5 summarizes the West Bank Interceptor (WBI) sanitary sewer overflows that occurred during the month of January. There were no West Bank Interceptor (WBI) SSOs experienced in February or March. The failure of the aerial crossing at Hanging Moss Creek has been mitigated with the bypass pumping arrangement. Work is underway to construct a permanent repair.

Finally, Table A-14 details the pump station SSO events that occurred in March. No pump station SSO events were reported for the months of January and February.

1.2 Prohibited Bypasses

There were no prohibited bypasses experienced by the system during this reporting period.

Section 2: Narrative Report

Because of a chronic failure to properly operate the Sewer System over a period of years, on September 30, 2023, the U.S. District Court for the Southern District of Mississippi entered a Stipulated Order on the Sewer System and appointed an Interim Third-Party Manager, Edward “Ted” Henifin, and JXN Water to maintain the City of Jackson, MS Sewer System. This quarterly report summarizes activities affecting the operation of the Sanitary Sewer System serving the City of Jackson, Mississippi during the 1st quarter of 2026.

2.1 Projects and Activities

JXN Water staff evaluates all the sewer calls that are received by the call center. All locations of concern are promptly visited and evaluated to identify any public sewer-related issues. JXN Water hired Closed Circuit Television (CCTV) and construction contractors to help address the sewer issues found throughout the City of Jackson, Mississippi.

In the Queens area sewer, approximately 48,987 linear feet (LF) of pipes have been cleaned and/or televised since the stipulated order went into effect. 47 sewer repair locations and 2,368 LF of cured-in-place pipe (CIPP) have been completed in the Queens sewer area by the JXN Water Sewer Team since the effective date of the stipulated order.

Systemwide, approximately 105,478 LF of sewer were assessed and, as necessary, cleaned this quarter through the annual sewer cleaning and CCTV contract. Since JXN Water has been responsible for sewer, a total of approximately 1,394,733 LF have been assessed and addressed to date.

All of the 2,200 service requests referenced in the Stipulated Order have been evaluated. Sewer locations requiring repairs have either been made or are scheduled to be addressed.

Construction contractors have completed sewer failure repairs at 45 locations throughout Jackson this quarter. The total number of repaired sewer failure locations to date is 769. This figure includes emergency sewer failures as well as many unlisted locations due to priority of the issues presented. Not included in this figure are 13 manhole frame/lid repair/riser repairs completed this quarter. A total of 201 such repairs have been completed to date.

29,336 LF of CIPP have been completed to date. Approximately 6,300 LF of sewer line have been replaced by pipe bursting. During the pipe bursting process, our contractor also installed new service lateral taps that were tied into the system for these line segments.

Management, Operations and Maintenance (MOM) Plans

The ITPM submitted updated MOM Plans for agency review on September 29, 2024 in accordance with the terms of the Stipulated Order. These plans included the Gravity Line Maintenance Plan, the Sewer Overflow Response Plan, the Pump Station Operations and Maintenance Plan and the Fats, Oils and Grease Control Plan. USEPA issued an approval letter on December 20, 2024 for all updated plans except the Pump Station O&M Plan where there were two comments to address. The revised Pump Station O&M Plan incorporating USEPA comments has been submitted for agency review.

2.2 Delays

JXN Water does not have sufficient funding to support the needed capital investments to fulfill its obligations under the Stipulated Order. Although a rate increase has been approved, it will take some time to implement the increase and build up funds to support the capital program. Delays on meeting schedule obligations under the Stipulated Order are likely.

2.3 Sewer Project Priority List and Implementation Schedule

The ITPM submitted an updated list of Priority Projects and their associated implementation schedule on December 18, 2024 in accordance with the terms of the Stipulated Order. The implementation schedule is contingent upon acquiring adequate funding for each of the projects. The schedule is also contingent upon the United States Army Corps of Engineers (USACE) where Section 219 funding is being used. USEPA approved the list and schedule on December 20, 2024.

An updated implementation schedule for the Priority Projects is shown in Table 1 below. Please note that completion dates are dependent on securing capital funding on a timely basis and subject to change based on actual receipt of funds. No changes to this table are noted from previous quarterly report. Unless a rate increase is approved very soon, the schedules shown below will be delayed.

Table 1. JXN Water Master Schedule for Priority Projects		
Priority Ranking	Project Name	Project Description
1	Queens Area Sewer Rehabilitation Project	Rehabilitation of the sewers within the Queens Project Area 3-6 focusing on, but not necessarily limited to, dry weather SSO reduction and point repairs to address sewer line collapses.
Original Projection - Completion 12/31/2025		COMPLETED.
2	Emergency Sewer Failures	Complete cleaning and closed-circuit television (CCTV) for the rehabilitation and/or replacement of the Emergency Sewer Failure locations listed in Appendix C.
Original Projection - Completion 12/31/2025		Actual Completion 12/31/2024
3	Annual Sewer Cleaning & CCTV Contract	Contract for annual sewer cleaning and CCTV, and complete 100 miles/year. Coordinate this annual cleaning and CCTV work with the prioritized Service Request Investigations below.
Original Projection - Completion 12/31/2024		Contract is in place and cleaning and inspection will be ongoing throughout the term of the Order.
4	Investigate Service Request Locations	Contract an annual investigation of sewer issues coming from the 2,200 Service Request locations and coordinate cleaning and CCTV with the Annual Sewer Cleaning & CCTV Contract above.
Original Projection - Completion 12/31/2024		Actual Completion 12/31/2024
5	Mill Street Sewer Rehabilitation Project	Re-route 2,200 linear feet of sewer that crosses a railroad (RR) yard, where the sewer line has collapsed underneath the RR tracks. A new sewer line will be constructed around the RR yard and the existing sewer line will be filled with flowable fill and abandoned in place.
Original Projection - Reevaluation complete 12/31/2024.		Reevaluation has been completed. Pump station and gravity pipe options evaluated. Gravity pipe selected. Reroute approximately 2200 linear feet(1f) of 15" sewer line under railroad (RR) yard and replace with approximately 5000 lf of 24" gravity sewer along Mill Street. Abandon existing sewer in RR yard. Estimated substantial completion July 30, 2026. This schedule is unlikely to be achieved because of a lack of funding.
6	West Bank Interceptor Rehabilitation	Complete the cleaning and rehabilitation of the West Bank Interceptor (WBI) for Project 6 Segment Phase (MH IT0118 to MH IT0136). This repair will address the low manhole that is believed to be a major contributing source of inflow during a river stage in excess of 26 ft. The project will also address any needed grouting work of the interceptor and manholes in the Country Club area of the WBI. Identify additional major river water inflow locations and defects causing significant volumes during a river stage above 26 ft. Develop and implement the repair plan, including a schedule of implementation.

Original Projection - Reevaluation complete 12/31/2024.		Reevaluation is complete. Clean approximately 8600 lf of 48" and 54" sewer, CIPP approximately 700 lf of sewer from MH IT0118 to IT0120 and rehabilitate 38 manholes that have significant inflow defects and/or are impacted by flooding at river stage 26. Estimated substantial completion August 30, 2026. This schedule is unlikely to be achieved because of a lack of funding.
7	Savanna WWTP 100 MGD Peak Flow Wastewater Pump	Replace the 100 million gallons per day (MGD) Peak Flow Pump that discharges flow from the Influent Pump Station to the Stormwater Lagoon cells.
Original Projection Completion 9/30/2026		USACE to purchase and install new pump with VFD. Estimated substantial completion October 30, 2026
8	Savanna WWTP Emergency Repairs/Replace Dewatering Equipment	Replace 54-inch line from inside Influent Pump Station to Headworks, replace return activated sludge (RAS) Pump # 2, and install permanent dewatering equipment to eliminate monthly cost for renting two belt filter presses.
Original Projection - Reevaluation Completion 12/31/2024		Reevaluation complete. Elements include: • Replace trash screens with automated bar screens • Repair and rehabilitate IPS wet well • Repair 84-in force main • Correct hydraulic issues including effluent channel opening in Anoxic Basin • Replace SC4 mechanism • Construct SC6 and install 3rd RAS pump in RAS PS 2 • Replace gravity thickener mechanisms (2 units) • Procure/install new trailer mounted belt presses (2 units) Estimated substantial completion February 28, 2028.
9	Savanna Peak Cell Lagoon Cells	Clean out the three peak flow lagoon cells at the Savanna WWTP.
Original Projections - Completion 10/31/2026		Estimated Substantial Completion July 31, 2028
10	Trahan WWTP Rehabilitation	Conduct a Comprehensive Performance Evaluation and a Composite Correction Program (CCP) for the Trahan WWTP. Implement the CCP as schedule permits. Make immediate repairs to maintain operations as needed.
Original Projection - CCP Complete 12/31/2025 Implementation schedule to be determined in CCP		Estimated Completion of CCP 12/31/2025. Implementation schedule to be included in CCP.
11	Savanna WWTP Phase 1B Type 2 Improvements	Construct new septage/Fat, Oils, and Grease (FOG) receiving station, rehabilitate one screw pump at the Effluent Pump Station, add 6th secondary clarifier, add new dewatering equipment, add covered sludge storage facilities along with new waste activated sludge (WAS) storage tank, construct new gravity thickeners, address structural deterioration in Influent Pump Stations, and rehabilitate the 84-inch line from Sludge Lagoons to Pump Station.
Original Projection- Reevaluation complete 12/31/2024. Construction complete TBD		Reevaluation has been completed. Most elements addressed in Project 8 above. New element to be constructed is additional dewatered cake storage. Estimated substantial completion is January 31, 2031.

2.4 Accounting of Expenditures

Table 2 below shows expenditures from the Sewer O&M account for January – March 2026, funded by the local revenues collected.

Table 2. JXN Water Expenditures vs. Budget for FY25

	ACTUAL	BUDGET	% OF BUDGET
Expenses			
Sewer Expenses			
Cleaning and Maintenance	\$1,648,677.00	\$7,200,000.00	22.90%
Metering – Sewer Expenses	\$56,299.50	\$260,000.00	21.65%
Plant O & M – Sewer	\$3,546,218.34	\$18,120,000.00	19.57%
Program Management	\$115,165.46	\$2,340,000.00	4.92%
Sewer Repairs	\$517,068.29	\$6,000,000.00	8.62%
Total Sewer Expenses	\$5,883,428.59	\$33,920,000.00	17.35%
Total Expenses	\$5,883,428.59	\$33,920,000.00	17.35%
Other Expenses			
Capital Projects			
ARPA – Large Repair Term Contract	\$163,518.70		
ARPA – Lining Contract	\$177,349.50		
ARPA – Small Repair Term Contract	\$70,476.00		
Sewer Mill St	\$163,518.70		
Total Capital Projects	\$675,575.66	\$0.00	
Total Other Expenses	\$675,575.66	\$0.00	

2.5 Projection of Work for Upcoming Quarter

JXN Water Sewer Cleaning and CCTV Contractors will continue to clean and televise the sewer system throughout the City. This work will focus on known issue locations that have not been previously evaluated. Also, new locations with issues called in by residents and businesses throughout the City will continue to be evaluated.

JXN Water will continue to prioritize sewer repairs based on the impacts it causes to its customers, first addressing overflows and backups to structures and sensitive properties (playground, schools, healthcare, and high traffic/safety issues). Note that the projected work for next quarter remains the same as the previous quarter until additional funding is secured. JXN Water plans to perform the following work during the next quarter:

- Clean and CCTV 25 miles of sewer throughout the city's sewer system.
- Perform approximately 15 construction sewer repairs in the City's sewer system.

Construction on the West Bank Interceptor (WBI)/Hanging Moss repair is expected to continue within the next quarter.

2.6 Supplemental Environmental Program (SEP)

The SEP was closed out during the 4th Quarter of 2025.

2.7 Trends Analysis

As part of the requirements of the Stipulated Order, a Trends Analysis is required for this Quarterly Reporting period to cover the period of January 2024 through December 2025. The trends analysis must include the number, volume, duration, and cause of sanitary sewer overflows and prohibited bypasses for the two preceding calendar years. This analysis includes only events that occurred in municipally owned infrastructure, and during the months of January 2024 through December 2025.

Figure 2-1 shows the total number of SSO events that occurred during each month of the analyzed period. The number of SSO events clearly trends down over the past two calendar years.

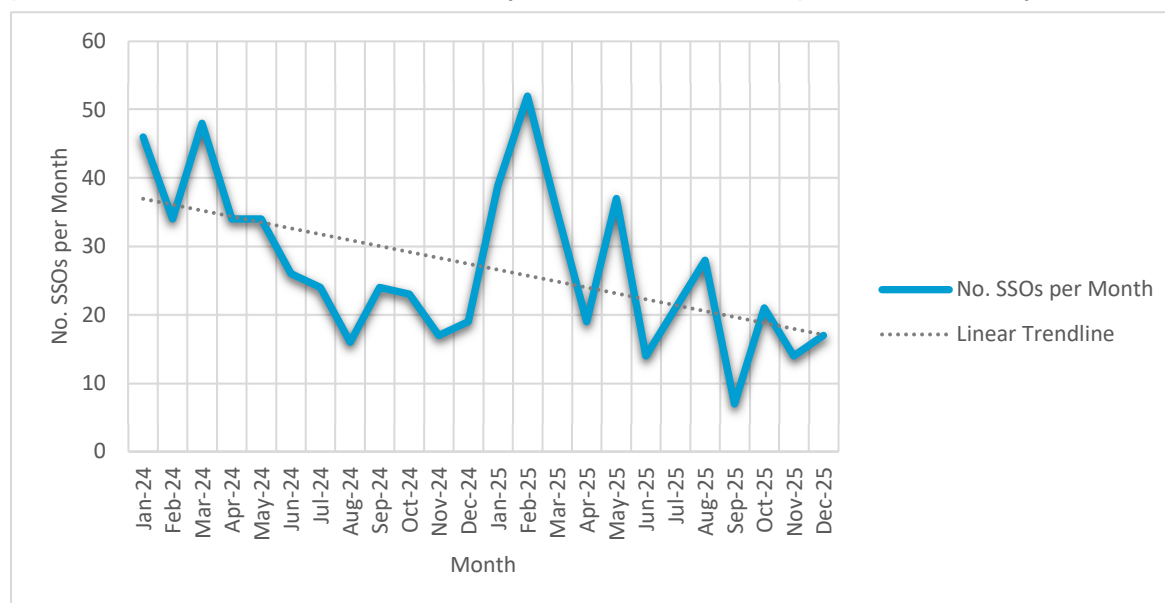


Figure 2-1. Number of Municipally Owned Sanitary Sewer Overflows by Month

Figure 2-2 shows the total estimated volume in gallons of all SSO events during each month of the analyzed period.

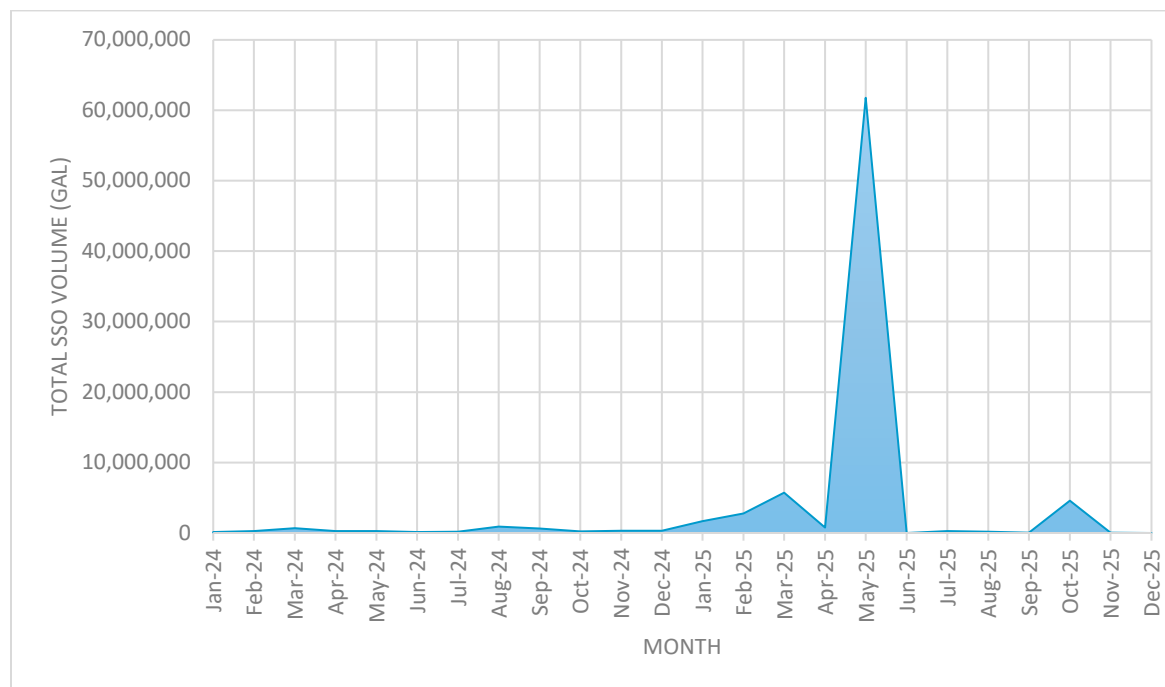


Figure 2-2. Total Volume of Municipally Owned Sanitary Sewer Overflows by Month

Figure 2-3 shows the average duration of SSO events each month during the reporting period. The average duration of SSO events is clearly trending down over the past two calendar years.

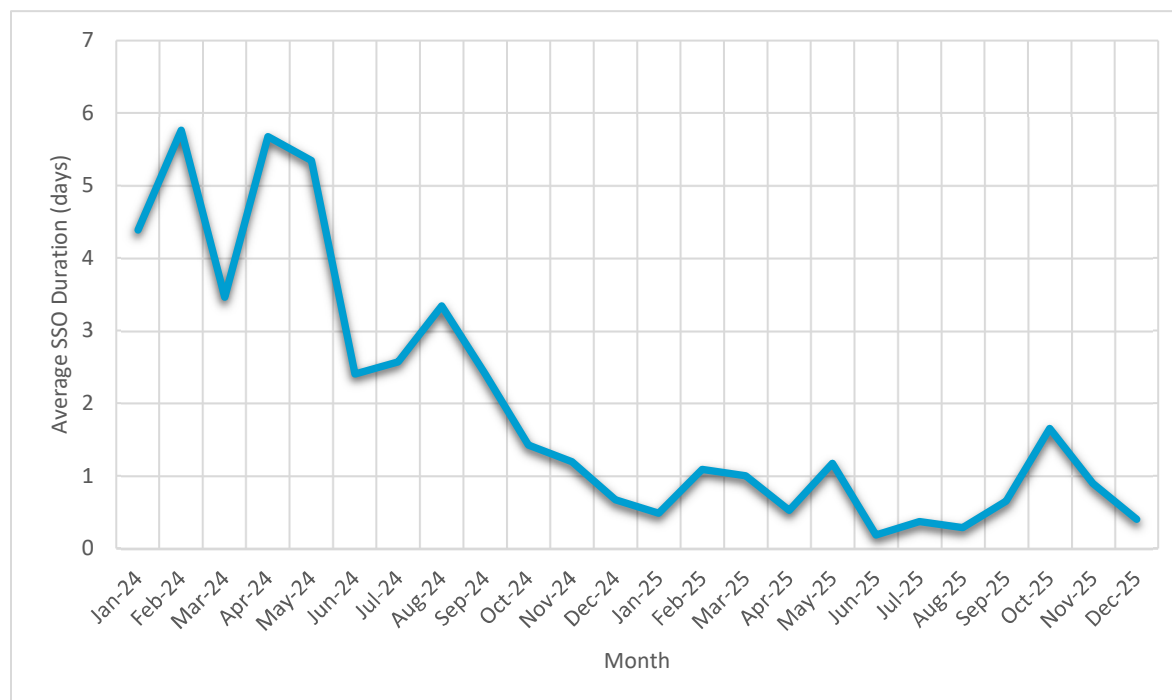


Figure 2-3. Average Duration of Sanitary Sewer Overflows by Month

Figure 2-4 shows the causes of sanitary sewer overflows in municipally owned infrastructure during the entire analyzed period of January 2024 to December 2025 by percentage. Grease, solids, rags, and debris were the most common known cause of sanitary sewer over two years.

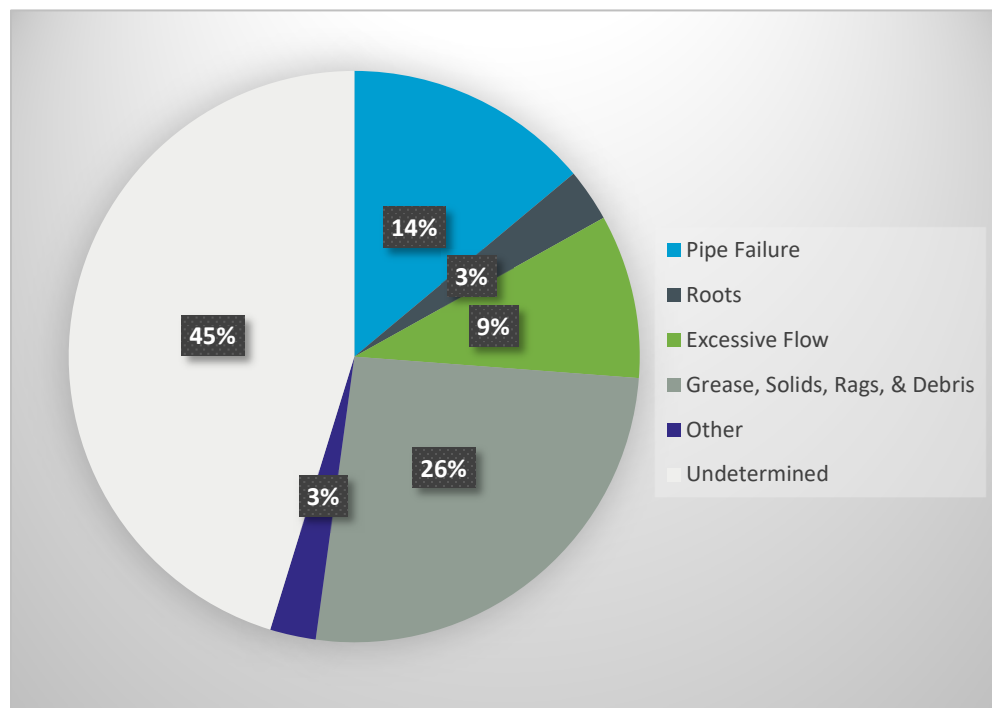


Figure 2-4. Causes of Municipally Owned Sanitary Sewer Overflows during 2024-2025

Figure 2-5 shows the number of sanitary sewer overflows in municipally owned infrastructure for each month of the analyzed period by cause.

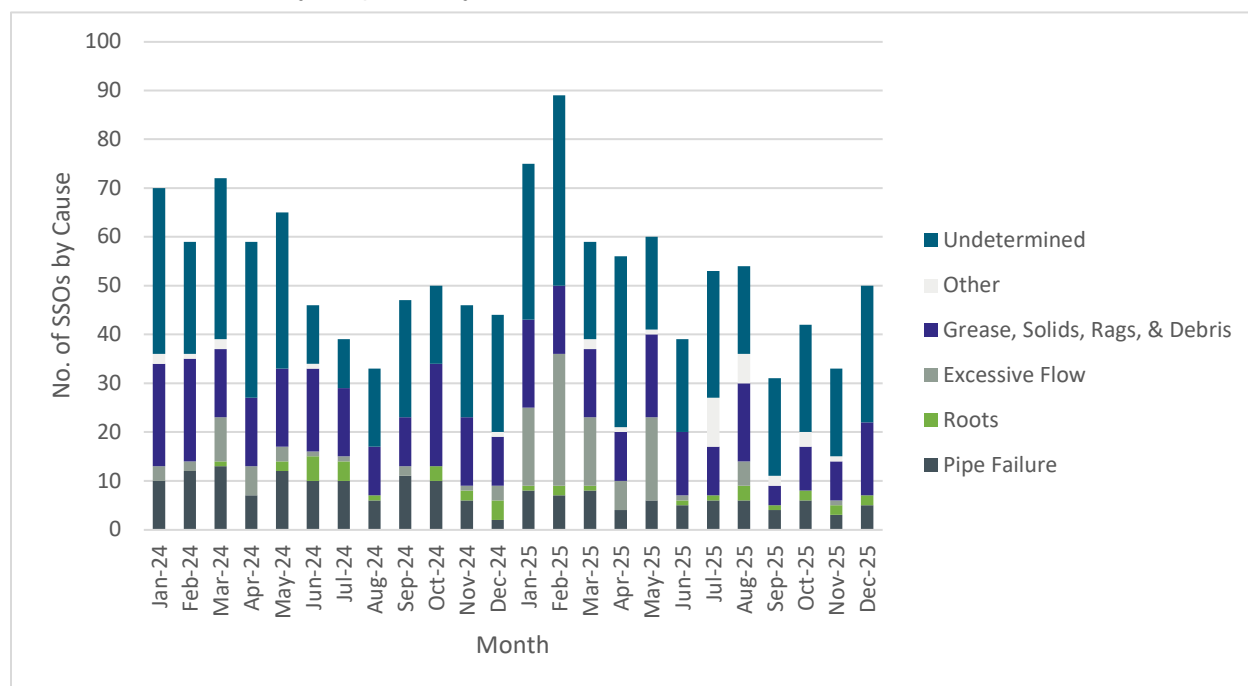


Figure 2-5. Causes of Municipally Owned Sanitary Sewer Overflows by Month

Figure 2-6 shows the number of prohibited bypass events from the Savanna WWTP storm lagoon for each month of the analyzed period by cause. There have been no prohibited bypass events since May 2024.

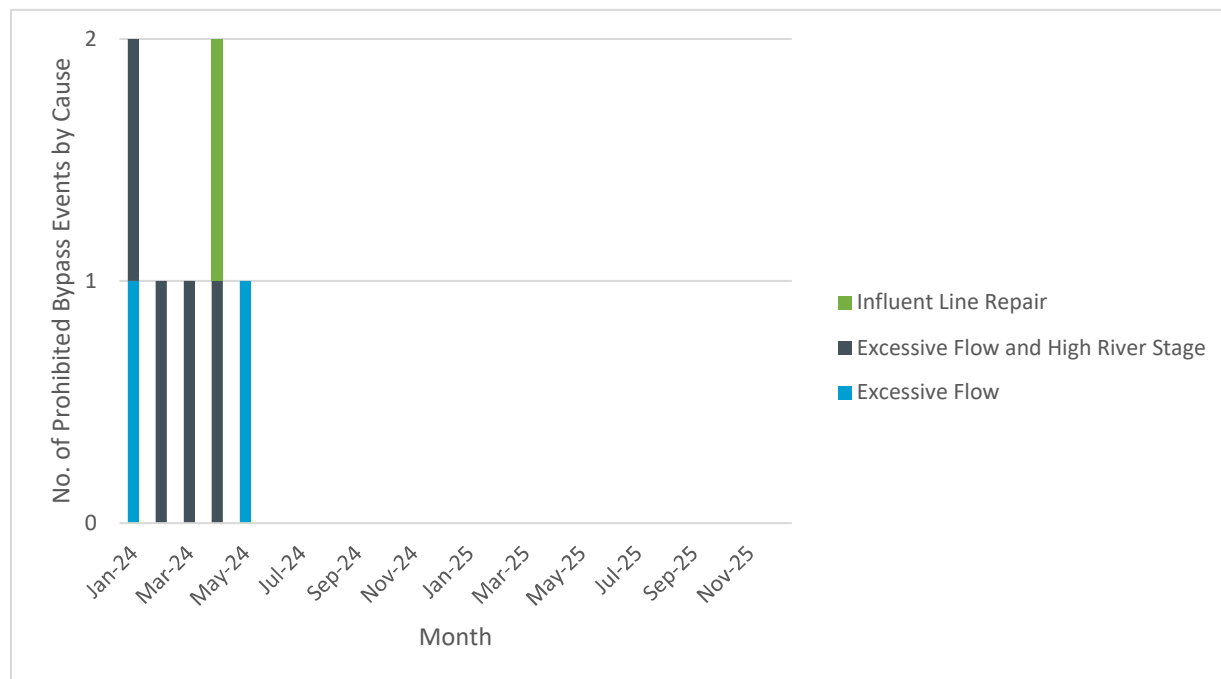


Figure 2-6. Causes of Prohibited Bypass Events by Month

Figure 2-7 shows the total estimated volume in gallons of prohibited bypass events at the Savanna WWTP for each month of the analyzed period. No flow has been discharged via prohibited bypass events since May 2024.

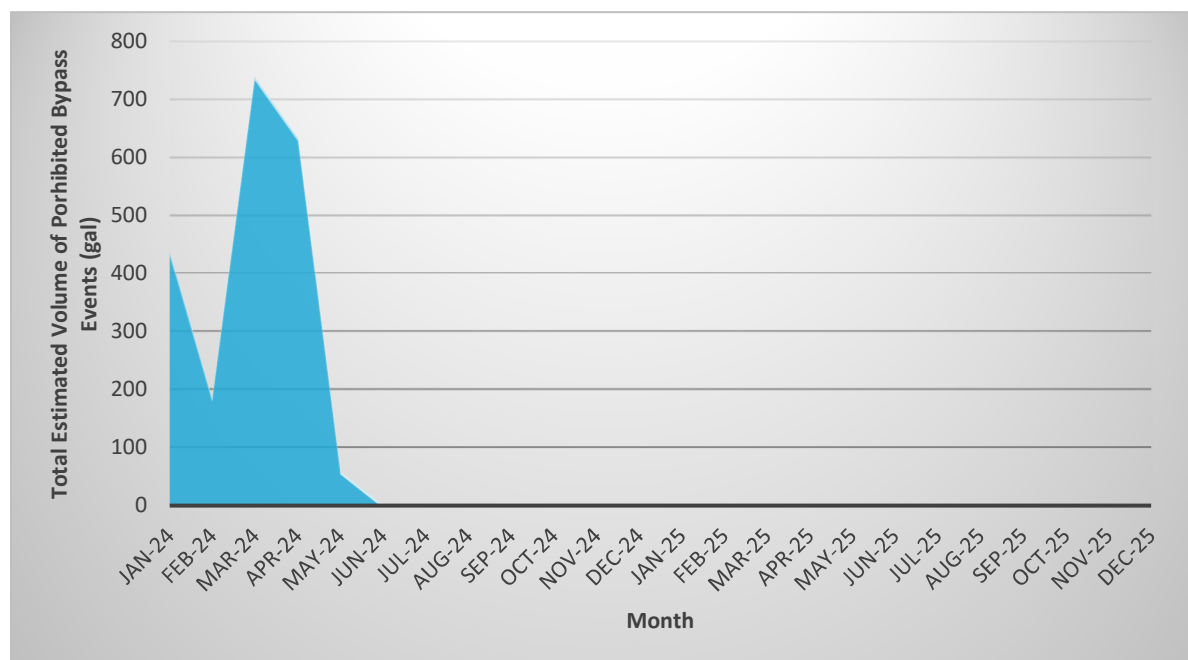


Figure 2-7. Total Estimated Volume of Prohibited Bypass Events by Month

Figure 2-8 shows the total duration of prohibited bypass events at the Savanna WWTP for each month of the analyzed period.

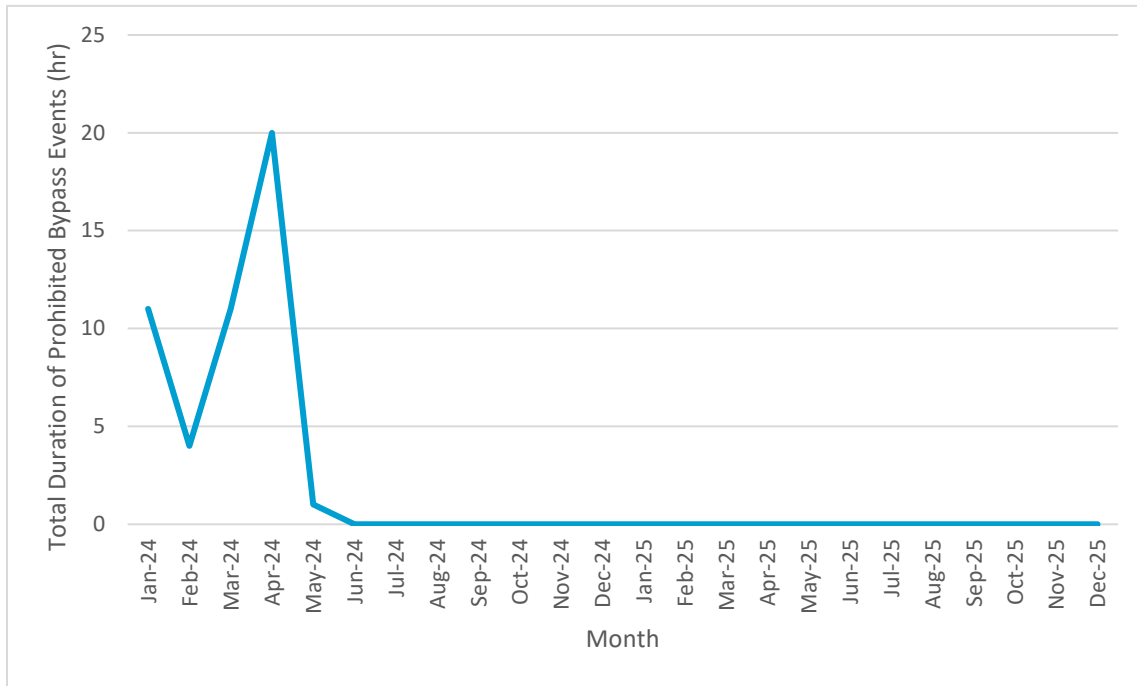


Figure 2-8. Total Duration of Prohibited Bypass Events by Month

Appendix A: Collection System SSO Data

Table A-1. Municipally Owned January Collection System SSOs which Reached Waters of the State

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
10/15/25 1:01 PM	LIVINGSTON ST	Ground Surface (defective pipe underground)	31	310,000	YES	Town	Municipal	Collapsed Pipe	SSO Ongoing
1/5/26 4:57 PM	324 W NORTHSIDE DR	Manhole	0.10	89	YES	Eubanks	Municipal	Solids	SSO Stopped
1/16/26 11:26 AM	NORTHSIDE DR	Manhole	0.12	242	YES	Eastover	Municipal	Grease	SSO Stopped
1/20/26 9:02 AM	140 ELM CT	Manhole	0.19	938	YES	Town	Municipal	Solids	SSO Stopped
1/20/26 10:11 AM	3173 W NORTHSIDE DR	Manhole	0.22	327	YES	Town	Municipal	Grease	SSO Stopped
1/26/26 1:34 PM	2240 WESTBROOK DR	Ground Surface (defective pipe underground)	0.06	604	YES	Hanging Moss	Municipal	Collapsed Pipe	SSO Stopped
1/27/26 5:47 PM	1525 ELLIS AVE	Manhole	0.13	1,250	YES	Lynch	Municipal	Grease	SSO Stopped
1/28/26 10:10 AM	2951 LAKEWOOD DR	Manhole	0.17	253	YES	Cany	Municipal	Solids	SSO Stopped
1/31/26 11:20 AM	905 ELLIS AVE	Manhole	0.53	1,056	YES	Lynch	Municipal	Collapsed Pipe	SSO Ongoing
1/31/26 12:07 PM	802 PRIMOS AVE	Ground Surface (defective pipe underground)	0.50	495	YES	Lynch	Municipal	Collapsed Pipe	SSO Ongoing

Table A-2. Municipally Owned January Collection System SSOs which Did Not Reach Waters of the State

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
1/5/26 2:50 PM	5444 CLINTON BLVD	Ground Surface (defective pipe underground)	1.04	416	NO	Lynch	Municipal	Solids / Collapsed Pipe	SSO Stopped
1/5/26 4:22 PM	3858 REDBUD RD	Manhole	0.07	52	NO	Eubanks	Municipal	Solids	SSO Stopped
1/6/26 11:50 AM	5441 WILLIAMS DR	Cleanout	0.16	49	NO	Lynch	Municipal	Solids	SSO Stopped

1/23/26 8:55 AM	2332 TWIN LAKES CIR	Cleanout	0.22	66	NO	Eastover	Municipal	Solids	SSO Stopped
1/28/26 11:12 AM	WILLOW WAY	Manhole	0.15	226	NO	Three Mile	Municipal	Solids	SSO Stopped
1/28/26 4:09 PM	2811 UTAH ST	Ground Surface (defective pipe underground)	0.05	107	NO	Town	Municipal	Solids	SSO Stopped
1/29/26 5:27 PM	5913 FLORA ST	Manhole	0.05	264	NO	Hanging Moss	Municipal	Solids	SSO Stopped
1/30/26 5:23 PM	107 PINE ISLAND DR	Cleanout	0.06	19	NO	Hanging Moss	Municipal	Solids	SSO Stopped
1/30/26 6:09 PM	1945 WILLANEEL DR	Cleanout	0.81	483	NO	Three Mile	Municipal	Solids	SSO Stopped

Table A-3. January Frontage Rd Collapse SSO Details

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
10/17/25 8:00 AM	6103 W FRONTAGE RD	Ground Surface (defective pipe underground)	31	9,299,997	NO	White Oak	Municipal	Collapsed Pipe	SSO Ongoing*

* - Although the pipe is still collapsed and the SSO is ongoing, the flow is contained and flows back into the collection system.

JXN Water has identified the following SSOs from privately owned infrastructure. JXN Water is not responsible for these SSOs and notifies the property owners that they need to address these problems.

Table A-4. Privately Owned January Collection System SSOs

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
1/5/26 10:12 AM	708 CEDARHURST DR	Cleanout	0.00	-	NO	Hanging Moss	Private	Undetermined	SSO Stopped
1/5/26 11:30 AM	2725 N WEST ST	Cleanout	26.52	7,956	NO	Town	Private	Undetermined	SSO Ongoing
1/5/26 1:14 PM	249 ARCHER AVE	Ground Surface (defective pipe underground)	26.45	7,935	NO	Cany	Private	Undetermined	SSO Ongoing
1/6/26 10:55 AM	143 PIMLICO PL	Cleanout	25.55	7,664	NO	Hanging Moss	Private	Undetermined	SSO Ongoing
1/7/26 12:16 PM	2990 COLEMAN AVE	Ground Surface (defective pipe underground)	24.49	7,347	NO	Town	Private	Undetermined	SSO Ongoing
1/7/26 1:11 PM	230 MERRIMACK ST	Cleanout	24.45	7,335	NO	Lynch	Private	Undetermined	SSO Ongoing
1/7/26 1:46 PM	5821 OLD CANTON RD	Cleanout	24.43	7,328	NO	Purple	Private	Undetermined	SSO Ongoing
1/7/26 3:14 PM	176 W WOODCREST DR	Cleanout	0.00	-	NO	Cany	Private	Undetermined	SSO Stopped
1/8/26 8:43 AM	1106 AME LOGAN ST	Cleanout	23.64	7,091	NO	Lynch	Private	Undetermined	SSO Ongoing
1/9/26 2:13 PM	4659 DIXIE DR	Cleanout	22.41	6,722	NO	Lynch	Private	Undetermined	SSO Ongoing
1/9/26 9:35 PM	123 BRAZOS CIR	Cleanout	22.10	6,630	NO	Lynch	Private	Undetermined	SSO Ongoing
1/12/26 5:39 PM	5425 CLINTON BLVD	Manhole	0.14	1,444	NO	Lynch	Private	Solids	SSO Stopped
1/13/26 10:02 AM	2015 FLOWERS DR	Cleanout	0.03	8	NO	Hardy	Private	Solids	SSO Stopped

Quarterly Status Report

1/13/26 2:45 PM	3330 ELRAINE BLVD	Cleanout	0.03	9	NO	Town	Private	Solids	SSO Stopped
1/15/26 4:54 AM	1937 WILLANEEL DR	Cleanout	16.80	5,039	NO	Hanging Moss	Private	Undetermined	SSO Ongoing
1/15/26 8:06 AM	245 WILDWOOD TER	Cleanout	16.66	4,999	NO	Cany	Private	Undetermined	SSO Ongoing
1/15/26 1:51 PM	2105 BELVEDERE DR	Cleanout	0.18	54	NO	Three Mile	Private	Undetermined	SSO Stopped
1/15/26 2:36 PM	317 W NORTHSIDE DR	Cleanout	16.39	4,917	NO	Eubanks	Private	Undetermined	SSO Ongoing
1/15/26 6:02 PM	1151 MARBLE ST	Cleanout	0.00	-	NO	Cany	Private	Undetermined	SSO Stopped
1/15/26 6:54 PM	4676 NORDELL DR	Ground Surface (defective pipe underground)	16.21	4,864	NO	Hanging Moss	Private	Undetermined	SSO Ongoing
1/16/26 10:35 AM	4700 ROBINSON ROAD	Cleanout	0.02	7	NO	Lynch	Private	Undetermined	SSO Stopped
1/16/26 3:47 PM	5301 OLD CANTON RD	Cleanout	15.34	4,603	NO	White Oak	Private	Undetermined	SSO Ongoing
1/16/26 3:50 PM	723 W SILAS BROWN ST	Cleanout	15.34	4,602	NO	Town	Private	Undetermined	SSO Ongoing
1/17/26 3:23 PM	252 EASTVIEW ST	Cleanout	14.36	4,308	NO	Lynch	Private	Undetermined	SSO Ongoing
1/20/26 7:35 AM	2937 MARYDALE DR	Cleanout	11.68	3,505	NO	Cany	Private	Undetermined	SSO Ongoing
1/20/26 9:45 AM	1705 DEVINE ST	Cleanout	0.15	45	NO	Belhaven	Private	Undetermined	SSO Stopped
1/20/26 1:59 PM	2434 WILLIAMSON AVE	Cleanout	0.14	41	NO	Town	Private	Undetermined	SSO Stopped
1/21/26 11:24 AM	472 E NORTHSIDE DR	Cleanout	10.52	3,157	NO	Eubanks	Private	Undetermined	SSO Ongoing
1/22/26 11:24 AM	962 NORTH ST	Cleanout	9.52	2,857	NO	Town	Private	Undetermined	SSO Ongoing
1/24/26 7:36 AM	1233 TARA ROAD	Cleanout	0.00	-	NO	Cany	Private	Grease	SSO Stopped
1/24/26 12:59 PM	1838 NORTHWOOD CIR	Cleanout	0.00	-	NO	Hanging Moss	Private	Undetermined	SSO Stopped
1/27/26 8:14 PM	1510 ELLIS AVE	Manhole	4.16	41,569	YES	Lynch	Private	Grease	SSO Ongoing
1/28/26 9:47 AM	427 WILSHIRE AVE	Cleanout	3.59	1,078	NO	Eubanks	Private	Undetermined	SSO Ongoing
1/28/26 11:30 AM	4825 N STATE ST	Cleanout	3.52	1,056	NO	Eubanks	Private	Undetermined	SSO Ongoing
1/28/26 12:22 PM	5901 HWY 80 W	Cleanout	3.48	1,045	NO	Lynch	Private	Undetermined	SSO Ongoing
1/29/26 1:23 PM	304 E NORTHSIDE DR	Cleanout	2.44	733	NO	Eastover	Private	Undetermined	SSO Ongoing
1/29/26 2:10 PM	1504 SAINT CHARLES ST	Cleanout	2.41	723	NO	Town	Private	Undetermined	SSO Ongoing
1/30/26 1:41 PM	2024 MOBILE AVE	Cleanout	1.43	429	NO	Town	Private	Undetermined	SSO Ongoing
1/31/26 4:11 PM	1719 DEVINE ST	Cleanout	0.33	98	NO	Belhaven	Private	Undetermined	SSO Ongoing

Table A-5. January West Bank Interceptor (WBI) SSOs

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
1/9/26 5:00 PM	4686 E CHERYL DR	Manhole	0.25	25,000	YES	Hanging Moss	Municipal	Excessive Flow	SSO Stopped
1/25/26 4:00 PM	410 S JEFFERSON ST	Manhole	0.00	-	YES	Belhaven	Municipal	Excessive Flow	SSO Stopped
1/25/26 4:30 PM	3315 LAKELAND DR	Manhole	0.04	8,333	YES	Eubanks	Municipal	Excessive Flow	SSO Stopped
1/25/26 6:56 PM	4686 E CHERYL DR	Manhole	0.00	-	YES	Hanging Moss	Municipal	Excessive Flow	SSO Stopped

Table A-6. Municipally Owned February Collection System SSOs which Reached Waters of the State

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
10/15/25 1:01 PM	LIVINGSTON ST	Ground Surface (defective pipe underground)	28	280,000	YES	Town	Municipal	Collapsed Pipe	SSO Ongoing
1/31/26 12:07 PM	802 PRIMOS AVE	Ground Surface (defective pipe underground)	28	196,000	YES	Lynch	Municipal	Collapsed Pipe	SSO Ongoing
2/4/26 12:00 PM	2240 WESTBROOK DR	Ground Surface (defective pipe underground)	0.13	1,250,000	YES	Hanging Moss	Municipal	Collapsed Pipe	SSO Stopped
2/6/26 1:00 PM	905 ELLIS AVE	Manhole	0.00	-	YES	Lynch	Municipal	Collapsed Pipe	SSO Stopped
2/7/26 1:57 PM	4049 N WEST ST	Manhole	0.14	212	YES	Eubanks	Municipal	Collapsed Pipe	SSO Stopped
2/11/26 8:40 AM	1175 E COUNTY LINE ROAD	Ground Surface (defective pipe underground)	0.35	347	YES	Purple	Municipal	Grease	SSO Stopped
2/11/26 9:13 AM	905 ELLIS AVE	Manhole	1.29	259	YES	Lynch	Municipal	Seal Clamp	SSO Stopped
2/11/26 1:03 PM	1159 E NORTHSIDE DR	Manhole	0.19	111	YES	Eubanks	Municipal	Grease	SSO Stopped
2/18/26 1:25 PM	PEACHTREE ST	Manhole	0.19	193	YES	Belhaven	Municipal	Solids	SSO Stopped
2/21/26 10:52 AM	47 WOODY DR	Ground Surface (defective pipe underground)	0.14	109	YES	Cany	Municipal	Collapsed Pipe	SSO Stopped

Table A-7. Municipally Owned February Collection System SSOs which Did Not Reach Waters of the State

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
2/2/26 11:31 AM	345 SAINT ANDREWS DR	Ground Surface (defective pipe underground)	0.13	126	NO	Pearl	Municipal	Grease	SSO Stopped
2/4/26 8:25 AM	338 MEADOWOODS DR	Manhole	0.00	-	NO	Purple	Municipal	Excessive Flow	SSO Stopped
2/4/26 12:00 PM	2563 SHEPWOOD DR	Cleanout	0.15	44	NO	Three Mile	Municipal	Solids	SSO Stopped

2/4/26 1:36 PM	147 WINGED FOOT CIR	Ground Surface (defective pipe underground)	0.14	71	NO	Purple	Municipal	Collapsed Pipe	SSO Stopped
2/7/26 12:39 PM	530 DANIELS ST	Ground Surface (defective pipe underground)	0.02	5	NO	Lynch	Municipal	Grease	SSO Stopped
2/16/26 1:17 PM	158 MCDOWELL PARK CIR	Cleanout	0.07	34	NO	Cany	Municipal	Solids	SSO Stopped
2/18/26 3:05 PM	2010 N LAMAR ST	Cleanout	0.08	23	NO	Town	Municipal	Solids	SSO Stopped
2/19/26 2:16 PM	1391 N STATE ST	Manhole	0.06	1,687	NO	Belhaven	Municipal	Collapsed Pipe	SSO Stopped

Table A-8. February Frontage Rd Collapse SSO Details

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
10/17/25 8:00 AM	6103 W FRONTAGE RD	Ground Surface (defective pipe underground)	28	8,399,997	NO	White Oak	Municipal	Collapsed Pipe	SSO On-going*

* - Although the pipe is still collapsed and the SSO is ongoing, the flow is contained and flows back into the collection system.

JXN Water has identified the following SSOs from privately owned infrastructure. JXN Water is not responsible for these SSOs and notifies the property owners that they need to address these problems.

Table A-9. Privately Owned February Collection System SSOs

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
2/1/26 11:31 AM	219 CATALINA CIR	Cleanout	27.52	8,256	NO	Three Mile	Private	Undetermined	SSO Ongoing
2/2/26 3:44 PM	5216 ROMANY DR	Cleanout	26.34	7,903	NO	White Oak	Private	Undetermined	SSO Ongoing
2/5/26 4:06 PM	1741 GIBRALTAR DR	Cleanout	23.33	6,999	NO	Three Mile	Private	Undetermined	SSO Ongoing
2/5/26 4:56 PM	3039 FLEETWOOD DR	Cleanout	23.29	6,988	NO	Cany	Private	Undetermined	SSO Ongoing
2/5/26 5:20 PM	143 PIMLICO PL	Cleanout	0.00	-	NO	Hanging Moss	Private	Undetermined	SSO Stopped
2/6/26 8:06 AM	3625 HANCOCK ST	Cleanout	22.66	6,799	NO	Town	Private	Undetermined	SSO Ongoing
2/6/26 12:14 PM	1761 CAMELLIA LANE	Cleanout	22.49	6,747	NO	Lynch	Private	Undetermined	SSO Ongoing
2/7/26 11:06 AM	3844 HAWTHORN DR	Ground Surface (defective pipe underground)	0.24	73	NO	Eubanks	Private	Roots	SSO Stopped
2/9/26 1:26 PM	1431 SUMMIT DR	Cleanout	19.44	5,832	NO	Trahan	Private	Undetermined	SSO Ongoing
2/18/26 10:11 AM	6435 LYNDON B JOHNSON DR	Cleanout	10.58	3,173	NO	Bogue Chitto	Private	Undetermined	SSO Ongoing
2/18/26 1:15 PM	3506 HOLLYWOOD AVE	Cleanout	10.45	3,134	NO	Town	Private	Undetermined	SSO Ongoing

Quarterly Status Report

2/18/26 1:36 PM	1914 ROBINSON ST	Cleanout	10.43	3,130	NO	Lynch	Private	Undetermined	SSO Ongoing
2/18/26 1:49 PM	663 PIERMONT ST	Cleanout	10.42	3,127	NO	Eubanks	Private	Undetermined	SSO Ongoing
2/18/26 4:50 PM	915 OLEANDER AVE	Cleanout	10.30	3,090	NO	Three Mile	Private	Undetermined	SSO Ongoing
2/20/26 2:09 PM	3057 OXFORD AVE	Cleanout	8.41	2,523	NO	Town	Private	Undetermined	SSO Ongoing
2/23/26 1:47 PM	2221 SCANLON DR	Cleanout	5.43	1,628	NO	Hardy	Private	Undetermined	SSO Ongoing
2/26/26 3:20 PM	301 SEWANEE DR	Cleanout	2.36	708	NO	Lynch	Private	Undetermined	SSO Ongoing
2/27/26 12:13 PM	4317 PATCH AVE	Cleanout	1.49	447	NO	Lynch	Private	Undetermined	SSO Ongoing
2/27/26 1:02 PM	5645 PLEMON DR	Cleanout	1.46	437	NO	Hanging Moss	Private	Undetermined	SSO Ongoing
2/27/26 3:04 PM	1548 DIANNE DR	Cleanout	1.37	412	NO	Hardy	Private	Undetermined	SSO Ongoing
2/27/26 3:20 PM	1109 PALMYRA ST	Cleanout	1.36	408	NO	Town	Private	Undetermined	SSO Ongoing
2/28/26 11:59 AM	1705 LAUREL ST	Ground Surface (defective pipe underground)	0.50	150	NO	Lynch	Private	Undetermined	SSO Ongoing
2/28/26 3:48 PM	2852 FAIRHILL DR	Cleanout	0.34	102	NO	Hardy	Private	Undetermined	SSO Ongoing

Table A-10. Municipally Owned March Collection System SSOs which Reached Waters of the State

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
10/15/25 1:01 PM	LIVINGSTON ST	Ground Surface (defective pipe underground)	31.00	310,000	Yes	Town	Municipal	Collapsed Pipe	SSO Ongoing
1/31/26 12:07 PM	802 PRIMOS AVE	Ground Surface (defective pipe underground)	29.71	207,970	Yes	Lynch	Municipal	Collapsed Pipe	SSO Stopped
3/2/26 1:36 PM	3841 S SIWELL ROAD	Ground Surface (defective pipe underground)	0.14	2,736	Yes	Trahan	Municipal	Solids	SSO Stopped
3/12/26 11:53 AM	545 ROLLINGWOOD DR	Manhole	0.07	2,550	Yes	Hanging Moss	Municipal	Excessive Flow	SSO Stopped
3/17/26 2:00 PM	330 MEADOWWOOD DR	Manhole	0.00	-	Yes	Purple	Municipal	Excessive Flow	SSO Stopped
3/17/26 7:26 PM	1627 LOCKWOOD AVE	Manhole	0.05	1,700	Yes	Eastover	Municipal	Solids	SSO Stopped
3/19/26 7:05 PM	4209 OAKMONT DR	Manhole	0.08	2,875	Yes	Lynch	Municipal	Solids	SSO Stopped
3/21/26 9:38 PM	4931 SHADOW WOOD DR	Manhole	0.04	290	Yes	Hanging Moss	Municipal	Solids	SSO Stopped
3/24/26 10:23 AM	369 ROLLINGWOOD DR	Manhole	0.14	1,396	Yes	Hanging Moss	Municipal	Solids	SSO Stopped
3/24/26 11:58 AM	103 SAINT ANDREWS DR	Manhole	0.11	785	Yes	Purple	Municipal	Solids	SSO Stopped
3/25/26 10:04 AM	5517 CAHILL DR	Manhole	0.25	17,750	Yes	Lynch	Municipal	Grease	SSO Stopped

3/25/26 1:00 PM	2214 HERITAGE HILL DR	Ground Surface (defective pipe underground)	0.23	8,150	Yes	Hanging Moss	Municipal	Solids	SSO Stopped
3/27/26 1:22 AM	800 RAYMOND ROAD	Manhole	0.72	5,165	Yes	Three Mile	Municipal	Collapsed Pipe	SSO Stopped
3/27/26 7:23 AM	124 E SOUTH ST	Manhole	0.18	13,300	Yes	Town	Municipal	Solids	SSO Stopped
3/27/26 9:54 AM	322 S PRENTISS ST	Manhole	0.38	27,050	Yes	Town	Municipal	Collapsed Pipe	SSO Stopped
3/29/26 11:00 AM	124 E SOUTH ST	Ground Surface (defective pipe underground)	2.54	182,999	Yes	Town	Municipal	Collapsed Pipe	SSO Ongoing

Table A-11. Municipally Owned March Collection System SSOs which Did Not Reach Waters of the State

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
2/28/26 3:48 PM	2852 FAIRHILL DR	Cleanout	1.68	503	No	Hardy	Municipal	Grease	SSO Stopped
3/4/26 11:24 AM	2009 SOUTHBROOK RD	Ground Surface (defective pipe underground)	0.22	217	No	Eubanks	Municipal	Solids	SSO Stopped
3/4/26 2:38 PM	143 PRINCETON ST	Manhole	0.13	965	No	Town	Municipal	Solids	SSO Stopped
3/6/26 10:52 AM	2600 LAKELAND TER	Manhole	1.18	944	No	Eubanks	Municipal	Solids	SSO Stopped
3/7/26 9:52 AM	1704 WOODY DR	Manhole	0.00	-	No	Cany	Municipal	Excessive Flow	SSO Stopped
3/10/26 8:08 AM	1927 AMBLEWOOD DR	Manhole	0.15	5,500	No	Hanging Moss	Municipal	Collapsed Pipe	SSO Stopped
3/10/26 11:19 AM	40 GARDEN CIR	Manhole	1.08	32,542	No	Town	Municipal	Solids	SSO Stopped
3/11/26 2:10 PM	OUTER CIR	Manhole	2.14	64,312	No	Town	Municipal	Solids	SSO Stopped
3/12/26 5:18 PM	3330 ELRAINE BLVD	Ground Surface (defective pipe underground)	0.00	-	No	Town	Municipal	Excessive Flow	SSO Stopped
3/13/26 12:54 PM	160 MCTYRE AVE	Manhole	0.00	-	No	Town	Municipal	Excessive Flow	SSO Stopped
3/19/26 2:46 PM	2426 EASTOVER DR	Ground Surface (defective pipe underground)	0.20	158	No	Eastover	Municipal	Solids	SSO Stopped
3/19/26 5:52 PM	114 SWAN LAKE DR	Manhole	0.04	290	No	Trahan	Municipal	Solids	SSO Stopped
3/25/26 12:42 PM	4430 WILL O WOOD BLVD	Manhole	0.28	20,100	No	Trahan	Municipal	Solids	SSO Stopped
3/25/26 12:42 PM	4348 WILL O WOOD BLVD	Manhole	1.15	82,550	No	Trahan	Municipal	Collapsed Pipe	SSO Stopped
3/30/26 10:21 AM	7 MEADOWWOOD DR	Cleanout	0.21	148	No	Purple	Municipal	Grease	SSO Stopped
3/30/26 4:14 PM	3540 SUNSET DR	Manhole	0.17	6,200	No	Town	Municipal	Grease	SSO Stopped

Table A-12. March Frontage Rd Collapse SSO Details

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
----------------------------------	-----------------	-----------------	--------------------------	---------------------------------	-----------------------------	-----------------	----------------	----------------	------------

10/17/25 8:00 AM	6103 W FRONTAGE RD	Ground Surface (defective pipe underground)	31.00	9,299,996	No	White Oak	Municipal	Collapsed Pipe	SSO On-going*
------------------	--------------------	---	-------	-----------	----	-----------	-----------	----------------	---------------

* - Although the pipe is still collapsed and the SSO is ongoing, the flow is contained and flows back into the collection system.

JXN Water has identified the following SSOs from privately owned infrastructure. JXN Water is not responsible for these SSOs and notifies the property owners that they need to address these problems.

Table A-13. Privately Owned March Collection System SSOs

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Month Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
3/2/26 10:39 AM	252 EASTVIEW ST	Cleanout	29.56	8,867	No	Lynch	Private	Undetermined	SSO Ongoing
3/2/26 11:54 AM	109 SEGURA AVE	Ground Surface (defective pipe underground)	29.50	8,851	No	Lynch	Private	Undetermined	SSO Ongoing
3/3/26 11:30 AM	3308 SEARS ST	Cleanout	28.52	8,556	No	Town	Private	Undetermined	SSO Ongoing
3/3/26 12:53 PM	1195 MCDOWELL CIR	Cleanout	28.46	8,539	No	Hardy	Private	Undetermined	SSO Ongoing
3/3/26 3:53 PM	3560 JAYNE AVE	Cleanout	28.34	8,501	No	Lynch	Private	Undetermined	SSO Ongoing
3/4/26 10:47 AM	224 BRADLEY ST	Cleanout	27.55	8,265	No	Town	Private	Undetermined	SSO Ongoing
3/5/26 3:24 PM	1023 PARKWOOD PL	Cleanout	26.36	7,907	No	Eubanks	Private	Undetermined	SSO Ongoing
3/6/26 8:09 AM	641 N FLAG CHAPEL ROAD	Cleanout	25.66	7,698	No	Lynch	Private	Undetermined	SSO Ongoing
3/6/26 8:42 AM	1820 FIRST AVE	Cleanout	25.64	7,691	No	Lynch	Private	Undetermined	SSO Ongoing
3/6/26 10:54 AM	3002 N WEST ST	Cleanout	25.55	7,664	No	Town	Private	Undetermined	SSO Ongoing
3/6/26 2:27 PM	3808 CAMILLA DR	Cleanout	0.00	-	No	Cany	Private	Undetermined	SSO Stopped
3/9/26 8:54 AM	1021 NORTHPOINTE DR	Cleanout	0.00	-	No	Purple	Private	Undetermined	SSO Stopped
3/9/26 9:43 AM	4248 CYPRESS DR	Cleanout	22.60	6,779	No	Trahan	Private	Undetermined	SSO Ongoing
3/9/26 4:13 PM	228 S CANTON CLUB CIR	Cleanout	22.32	6,697	No	Purple	Private	Undetermined	SSO Ongoing
3/12/26 3:18 PM	150 WOODY DR	Manhole	19.36	139,410	No	Hardy	Private	Undetermined	SSO Ongoing
3/12/26 5:59 PM	1560 GIBALTAR DR	Cleanout	19.25	5,775	No	Lynch	Private	Undetermined	SSO Ongoing
3/17/26 4:39 PM	327 S PRENTISS ST	Cleanout	14.31	4,292	No	Lynch	Private	Undetermined	SSO Ongoing
3/18/26 12:02 PM	499 S PRESIDENT ST	Cleanout	13.50	4,050	No	Town	Private	Undetermined	SSO Ongoing
3/19/26 3:59 PM	2729 IDAHO ST	Cleanout	12.33	3,700	No	Town	Private	Undetermined	SSO Ongoing
3/21/26 7:48 AM	922 EASTVIEW DR	Cleanout	10.67	3,202	No	Lynch	Private	Undetermined	SSO Ongoing
3/23/26 5:10 PM	615 BRANDON AVE	Ground Surface (defective pipe underground)	8.28	2,485	No	Lynch	Private	Undetermined	SSO Ongoing
3/24/26 7:22 AM	4642 VILLAGE DR	Ground Surface (defective pipe underground)	7.69	2,308	Yes	Hanging Moss	Private	Undetermined	SSO Ongoing
3/24/26 8:35 AM	720 COOPER ROAD	Ground Surface (defective pipe underground)	7.64	2,293	No	Cany	Private	Undetermined	SSO Ongoing

3/24/26 9:05 AM	531 MERIGOLD DR	Ground Surface (defective pipe underground)	7.62	2,286	No	Three Mile	Private	Undetermined	SSO Ongoing
3/24/26 1:06 PM	2160 RAYMOND ROAD	Manhole	7.45	53,670	No	Cany	Private	Undetermined	SSO Ongoing
3/24/26 3:42 PM	1138 LYNCREST AVE	Cleanout	7.35	2,204	No	Belhaven	Private	Undetermined	SSO Ongoing
3/25/26 1:58 PM	128 & 132 DURAN VILLE	Cleanout	6.42	1,925	No	Trahan	Private	Undetermined	SSO Ongoing
3/27/26 3:30 PM	1010 CARNATION ST	Cleanout	4.35	1,306	No	Town	Private	Undetermined	SSO Ongoing
3/30/26 11:40 AM	2003 BELVEDERE DR	Cleanout	1.51	454	No	Three Mile	Private	Undetermined	SSO Ongoing
3/30/26 1:13 PM	3509 BISHOP AVE	Cleanout	1.45	435	No	Eubanks	Private	Undetermined	SSO Ongoing
3/31/26 12:55 PM	425 SYKES ROAD	Cleanout	0.46	139	No	Cany	Private	Undetermined	SSO Ongoing

Table A-14. March Pump Station SSOs

Date/Time SSO Originally Started	Location Street	Overflow Source	Estimated Duration, Days	Estimated Volume, Gallons	Reached Waters of the State	Receiving Water	Line Ownership	Reported Cause	SSO Status
3/7/2026 6:00 PM	6510 OLD CANTON RD	Manhole	0.27	5000	No	N/A	Municipal	High inflow and infiltration due to heavy rainfall	Complete/ended
3/9/2026 3:00 PM	166 MORSON RD	Manhole	24.25	500	No	N/A	Municipal	Broken pipe	Repaired/ended

Appendix B: White Oak (Frontage Road) SSO Photograph

